



MID-ATLANTIC
FISHERY MANAGEMENT COUNCIL

Program Review: Perspectives

Jessica Coakley

*Mid-Atlantic Fishery
Management Council*

October 17, 2024

Mid-Atlantic Fishery Management Council Program Review



JULY 2024

**THE PARNIN
GROUP**

Review Objective and Scope

- Primary objective to find innovative and efficient methods for Council to remain agile and responsive to new and evolving management challenges, including those related to climate change
- Identify opportunities to enhance the efficiency and adaptability of Council's processes, from early consideration of fishery management issues to the initiation of federal rulemaking



Project Oversight Team

- Council Staff (3):
Ecosystem, Habitat, Climate (+)
- NOAA Fisheries Greater Atlantic RFO (2):
Sustainable Fisheries, NEPA
- NOAA Fisheries Northeast FSC (3):
Ecosystems, Population Dynamics, Social Science Branch
- Group to help with proposal review and guide/advise work, review draft reports



Timeline

- Desire to get work completed prior to finalization of:
 - 5-year strategic plan, 2025 implementation plan, Regional Operating Agreement
- November 1, 2023, through July 31, 2024, presentation at August 2024 Meeting
- Everything was done well, but plan for more time!



Program Review Phases

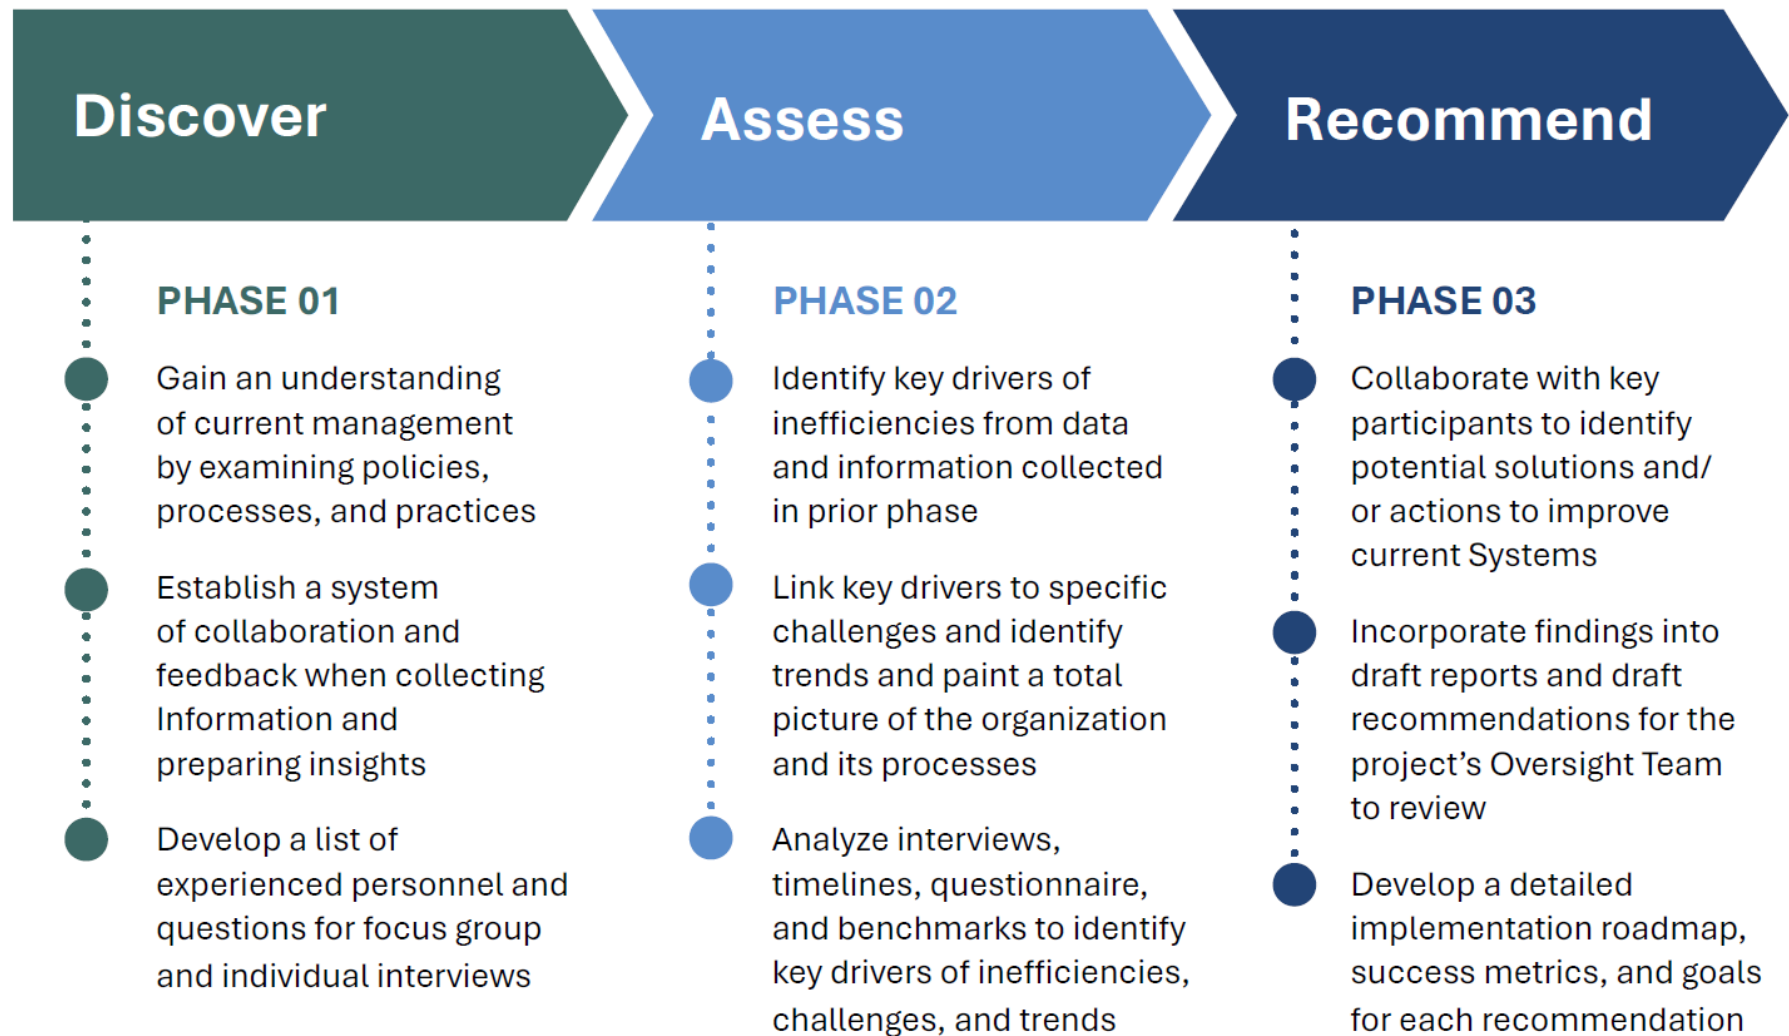


Figure 1. The Parnin Group's analytical approach.

Discover and Assess

- Parnin attended December Council Meeting to speak to attendees
- Attended other meetings virtually
- Conducted 10 focus groups, 6 individual Interviews, online questionnaire
- In total, interviewed 47 participants and received responses from 55 stakeholders
- OT worked closely with Parnin team to id 102 total contacts; provide context to connect findings with recommendations

| GROUP |
|-----------------------------|
| Council Member (voting) |
| Council Member (non-voting) |
| Council Staff |
| SSC |
| Advisory Panel Members |
| ASMFC Members |
| GARFO Members |
| NEFSC |
| TOTAL |

- » **Key Finding Category 1: Efficient and Flexible Management**
- » **Key Finding Category 2: Regulatory Process Documentation**
- » **Key Finding Category 3: Data Acquisition and Modeling**
- » **Key Finding Category 4: Climate Change Response**
- » **Key Finding Category 5: Coordination and Communication**



- **Anticipated Time Frame** - Long-term: greater than 5 years; Medium-term: 2 to 5 years; Short-term: less than 2 years.
- **Anticipated Task Complexity** - High: high degree of complexity with many considerations and complications, challenging to implement; Medium: somewhat complex, dependent on range of solutions, may be challenging to implement; Low: low degree of complexity, likely easy to implement.
- **Anticipated Impact on Process** - Increases flexibility (F); efficiency (E); and anticipation of climate change (C). High: could address all 3 criteria, Medium: meets 2 out of 3 criteria; Low: meets 1 of 3 criteria.



Recommendations Category 1: EFFICIENT AND FLEXIBLE MANAGEMENT

| RECOMMENDATION | ANTICIPATED TIMEFRAME | ANTICIPATED TASK COMPLEXITY | ANTICIPATED IMPACT ON PROCESS |
|---|-----------------------|-----------------------------|-------------------------------|
| R1. Limit Timeline for Scoping Actions/Development of Alternatives | Short-term | Low | Low (E) |
| R2. Develop Programmatic Environmental Impact Statement (PEIS) to Aid in the Development of Future Analyses | Long-term | High | High |
| R3. Reconsider Timelines and Frequency of Reviews | Medium-term | Low | Medium (F, E) |
| R4. Conduct a Framework Action Efficiency Analysis | Medium-term | Medium | Medium (F, E) |




Timeline Analysis and Benchmarking

Table 4. MAFMC action timeline analysis details (for 10 actions).


| STAGE ⁵ | AMENDMENT MEDIAN TIME | AMENDMENT TIME RANGE | FRAMEWORK MEDIAN TIME | FRAMEWORK TIME RANGE |
|--|--------------------------|-------------------------|--------------------------|-------------------------|
| 1. Initial (Scoping, Alternative development) | 24 months | 5-32 months | 12 months | 10-12 months |
| 2. Engagement and Review | 5 months | 4-7 months | 4 months | 4 months |
| 3. Council Transmittal | 10 months | 3-32 months | 9 months | 6-13 months |
| 4. NOAA final rule development | 3 months | 2-5 months | 2.5 months | 1-4 months |
| 5. Time from Council's final action to NOAA final rule | 14 months | 5-35 months | 11.5 months | 9-15 months |
| Total time taken | 41.5 months | 18-64 months | 24.5 months | 23-25 months |

Examples of Process/Communications Tools

MAFMC FMP and Major FMP Amendment Timeline

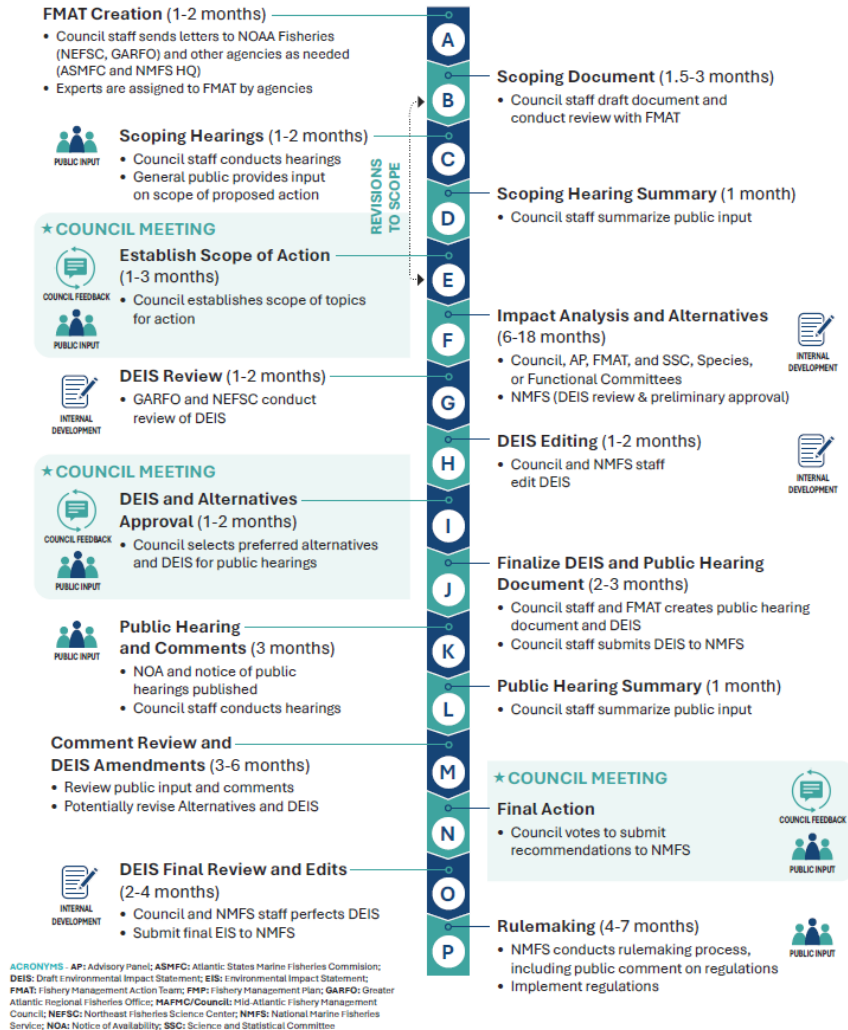

Typical Framework Action Timeline¹

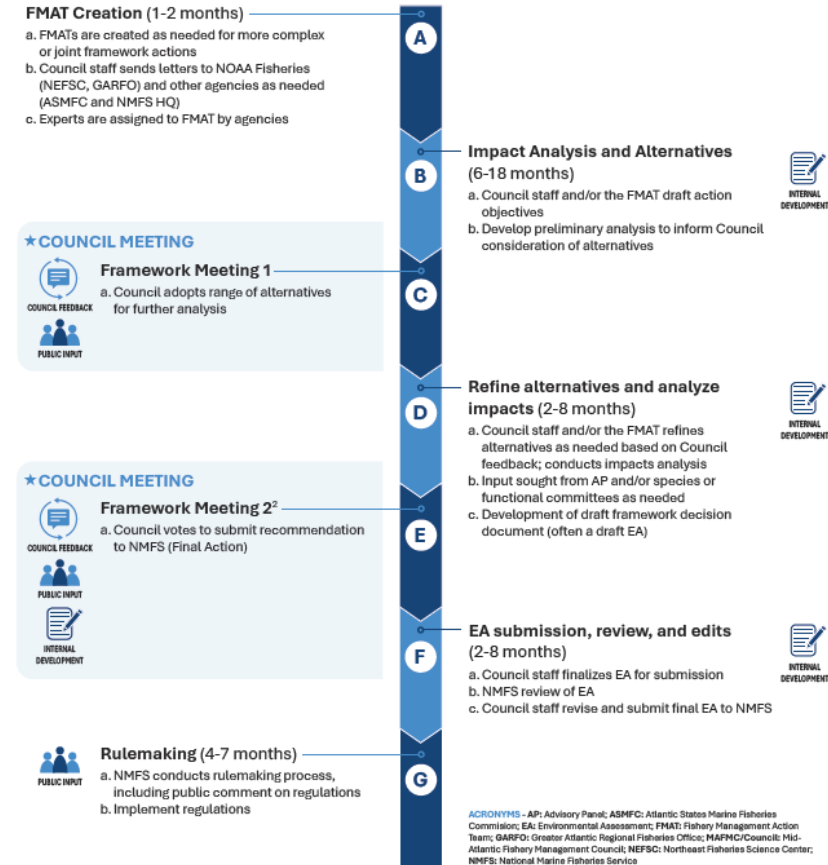


¹Typically a Council framework action does not include public hearings or a comment period. The Council may hold public hearings or a comment period per the ASMFC process if the framework action is part of a joint MAFMC-ASMFC action.

²More complex frameworks may take more than 2 Council meetings to reach final action.

My Overall Takeaways

- Report was well-received by Council
- Our Council staff are awesome! Input received reflected very positively on staff
- Need for better process communication tools
- Level of knowledge/perspectives about process from different groups was interesting to hear
- Room for improvement along a continuum from better staff resources to substantial fishery mgmt. process changes for Council

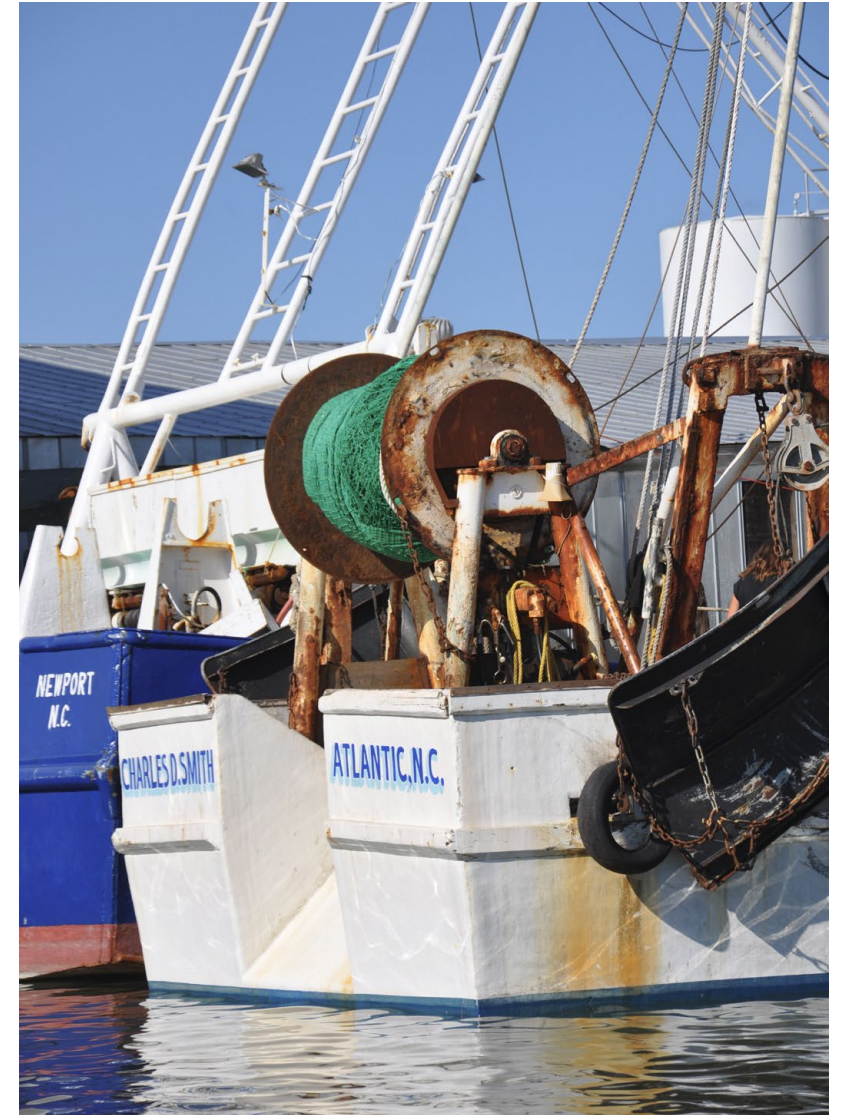

Next Steps

- Some recommendations included in MAFMC Strategic plan (2025-2029)
- And the 2025 implementation plan to direct Council/staff priorities
- Additional work under IRA planned to help more fully develop/implement recommendations



Questions about the project?

Jessica Coakley
Fishery Management Specialist
jcoakley@mafmc.org

Brett Wiedoff
The Parnin Group, Senior Consultant
Brett.Wiedoff@parningroup.com

Link to project description and report:
[here](#)

Extra thanks to MAFMC staff Kiley Dancy, Brandon Muffley, and NOAA Fisheries staff Marianne Randall, Emily Keiley, Sarah Gaichas, Anthony Wood, and Chad Demarest for their thoughtful feedback and guidance in this endeavor.

Report produced by Parnin Group in partnership with Lynker Corporation. **Funded by** MAFMC with support from NOAA Fisheries.
